

# Private

 Installer Copy

Job Name:

Customer Name:

Customer Address:

## Boxes Checklist:



Housing Unit

QTY: ☐

**\*\* QTY varies by build size**



Wall Pannel

QTY: 2 ☐



Tube And Bottom Bar

QTY: 2 ☐



Side Guide

QTY: 2 ☐



Side Covers

QTY: 2 ☐

Questions: Call: 718-782-7882




# Private

## Pre-Site Inspection Checklist


- ☐ Check for access to the Building, Loading Dock, Elevator, and Installation Room.
- ☐ Check the measurements of Installation Area to match with Shop Drawings.
- ☐ Lift Preparation, if needed.
- ☐ Check if there is enough space to work in the room.
- ☐ Determine what type of wall packing, and based on that, ensure you have the necessary hardware.
- ☐ Check Electricity, must install the motor side close to a plug or a 3-way wire.

## Sample Elevation View

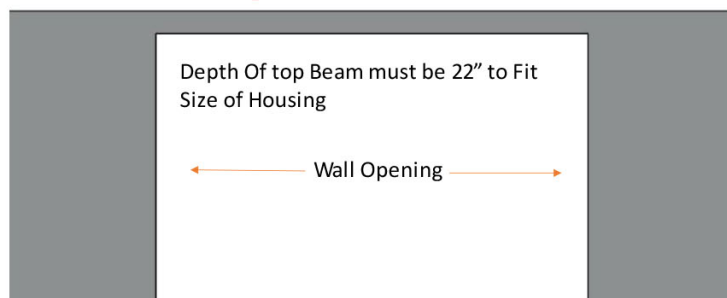

Site Requirements / Wall Opening PREP

- Top + Sides of the opening must be leveled prior To installation with laser leveler.
- Wall cannot be mounted to sheetrock.

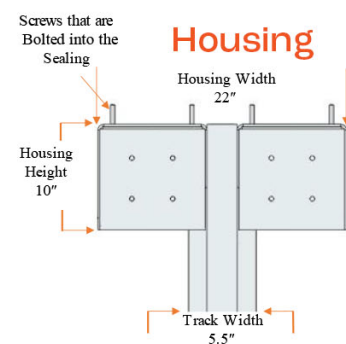

- Top + Sides of opening must have plywood backing or any hard packing.
- Remove any baseboard that might interfere with side guides installation.
